EXHIBIT C-2 - SCHEDULE

Phelan Road Widening
Work Order No. H15057
Project Schedule

ID	Task Name	Duration	Start	Finish	% Complete
1	**PROJECT MANAGEMENT**	**2038 day**	**Wed 6/9/21**	**Fri 3/30/29**	**49%**
2	Notice to Proceed	1 day	Wed 6/9/21	Wed 6/9/21	100%
3	Kick-Off Meeting	1 day	Wed 6/23/21	Wed 6/23/21	100%
4	**Project Management**	**2037 day**	**Thu 6/10/21**	**Fri 3/30/29**	**49%**
5	Project Management	2037 day	Thu 6/10/21	Fri 3/30/29	48%
6	Prepare Work Plan	23 days	Thu 6/10/21	Mon 7/12/21	100%
7	Prepare QA/QC Plan	23 days	Thu 6/10/21	Mon 7/12/21	100%
8	Project Development Team Meetings	2018 day	Wed 7/7/21	Fri 3/30/29	48%
9	**RESEARCH AND DATA COLLECTION**	**1863.4 d**	**Thu 6/10/21**	**Tue 8/1/28**	**64%**
10	Perform As-Built Research	10 days	Thu 6/10/21	Wed 6/23/21	100%
11	Perform Utility Research	124 days	Wed 6/23/21	Mon 12/13/21	100%
14	Perform Utility Coordination	670 days	Tue 1/6/26	Tue 8/1/28	0%
15	Field Reviews	10 days	Thu 6/24/21	Wed 7/7/21	50%
16	Perform Geotechnical Investigation	516 days	Wed 7/7/21	Wed 6/28/23	99%
47	Perform Design Survey and Right-of-Way Engineering	1007 day	Fri 7/23/21	Mon 6/2/25	75%
48	Perform Aerial Topographic Survey and Mapping	54 days	Fri 7/23/21	Wed 10/6/21	100%
49	Perform Ground Survey	71 days	Mon 8/23/21	Mon 11/29/21	100%
50	Prepare Right-of-Way Mapping	92 days	Fri 7/23/21	Mon 11/29/21	100%
51	Additional SR-138 and Phelan Road Topographic Survey and Mappi	63 days	Thu 8/4/22	Mon 10/31/22	100%
52	Additional Culvert Ground Survey	92 days	Fri 1/24/25	Mon 6/2/25	0%
53	Perform Potholing	70 days	Tue 1/6/26	Tue 4/14/26	0%
59	**PROJECT APPROVAL AND ENVIRONMENTAL DOCUMENT**	**1593.4 d**	**Thu 6/24/21**	**Tue 8/3/27**	**59%**
60	**Preliminary Engineering Studies**	**1183.4 d**	**Thu 6/24/21**	**Tue 1/6/26**	**87%**
61	Hydrology and Hydraulic Analysis	680 days	Thu 6/24/21	Wed 1/31/24	99%
96	Perform Traffic Analysis and Prepare Report	521 days	Wed 10/20/2	Wed 10/18/2	99%
122	SR-138 and Phelan Road Intersection	192 days	Wed 8/25/21	Thu 5/19/22	99%
131	Preliminary Culvert Layouts	359 days	Wed 2/14/24	Mon 6/30/25	92%
132	Confirming Headwall Locations with County	51 days	Wed 2/14/24	Wed 4/24/24	100%
133	Prepare Preliminary Culvert Layouts	106 days	Thu 4/25/24	Thu 9/19/24	100%
134	QA/QC Review and Revisions	5 days	Fri 9/20/24	Thu 9/26/24	100%
135	County Review - Preliminary Culvert Layout	37 days	Fri 9/27/24	Mon 11/18/24	100%
136	County Funding Review	38 days	Tue 11/19/24	Thu 1/9/25	100%
137	Culvert Review Meeting	1 day	Tue 12/10/24	Tue 12/10/24	100%
138	Update Preliminary Culvert Grading	20 days	Tue 6/3/25	Mon 6/30/25	0%
139	Prepare Geometric Design	954.4 da	Tue 12/14/21	Mon 8/11/25	90%
140	Prepare Existing Utility Base Mapping	12 days	Tue 12/14/21	Wed 12/29/2	100%
141	Prepare Geometric Design	30 days	Tue 12/14/21	Mon 1/24/22	100%
142	QA/QC Review and Revisions	10 days	Tue 1/25/22	Mon 2/7/22	100%
143	Geometric Design Presentation Meeting No. 1 - County	1 day	Tue 2/8/22	Tue 2/8/22	100%
144	County 1st Review - Geometric Design	30 days	Thu 3/3/22	Tue 11/1/22	100%
145	Coordinate and Resolve Comments with County	94 days	Wed 4/13/22	Mon 8/22/22	100%
146	Update Geometric Design	70 days	Tue 8/23/22	Mon 11/28/22	100%
147	QA/QC Review and Revisions	3 days	Tue 11/29/22	Thu 12/1/22	100%
148	County 2nd Review and Tentative Approval - Geometric Design	137 days	Fri 12/2/22	Mon 6/12/23	100%
149	Prepare Preliminary Roadway Centerline Profile and Grading	99 days	Thu 4/25/24	Mon 7/14/25	70%
150	QA/QC Review and Revisions	5 days	Mon 7/14/25	Mon 7/21/25	0%
151	County Review and Approval - Preliminary Roadway Centerline Pr	15 days	Mon 7/21/25	Mon 8/11/25	0%
152	Prepare 35% Plans and Estimate	106 days	Mon 8/11/25	Tue 1/6/26	0%
153	Prepare Draft Bridge Type Selection Report	20 days	Mon 8/11/25	Mon 9/8/25	0%
154	Prepare 35% Bridge Plans	40 days	Mon 8/25/25	Mon 10/20/25	0%
155	Prepare 35% Roadway Plan and Profile	60 days	Mon 8/11/25	Mon 11/3/25	0%
156	Prepare 35% Drainage Plans	40 days	Mon 8/25/25	Mon 10/20/25	0%
157	Prepare Preliminary WQMP	20 days	Mon 9/8/25	Mon 10/6/25	0%
158	Prepare 35% Cost Estimate	15 days	Mon 11/3/25	Mon 11/24/25	0%
159	QA/QC Review and Revisions	10 days	Mon 11/24/25	Mon 12/8/25	0%
160	35% Plans and Estimate Submittal Meeting - County and Caltrans	1 day	Mon 12/8/25	Tue 12/9/25	0%
161	County and Caltrans Review - 35% Plans and Estimate	20 days	Tue 12/9/25	Tue 1/6/26	0%
162	**Environmental Studies and Draft Environmental Document**	**1348.4 d**	**Thu 1/20/22**	**Tue 3/23/27**	**33%**
163	Prelimiarny Environmental Study (PES) - County Prepared	98 days	Thu 1/20/22	Mon 6/6/22	100%
166	Right-of-Entry Letters	107 days	Mon 9/26/22	Tue 2/21/23	99%
178	Environmental Focus Meeting	1 day	Mon 8/11/25	Tue 8/12/25	0%
179	Prepare Project Description	15 days	Tue 8/12/25	Tue 9/2/25	0%
180	QA/QC Review and Revisions	3 days	Tue 9/2/25	Fri 9/5/25	0%
181	County and Caltrans Review and Approval - Project Description	15 days	Fri 9/5/25	Fri 9/26/25	0%
182	Prepare Technical Studies	1176.4 d	Thu 2/3/22	Fri 8/7/26	28%
183	Air Quality Report, Air Quality Conformity Analysis and GHG Asse	50 days	Fri 9/26/25	Fri 12/5/25	0%
184	MGS Habitat Assessment	3 days	Thu 2/17/22	Mon 2/21/22	100%

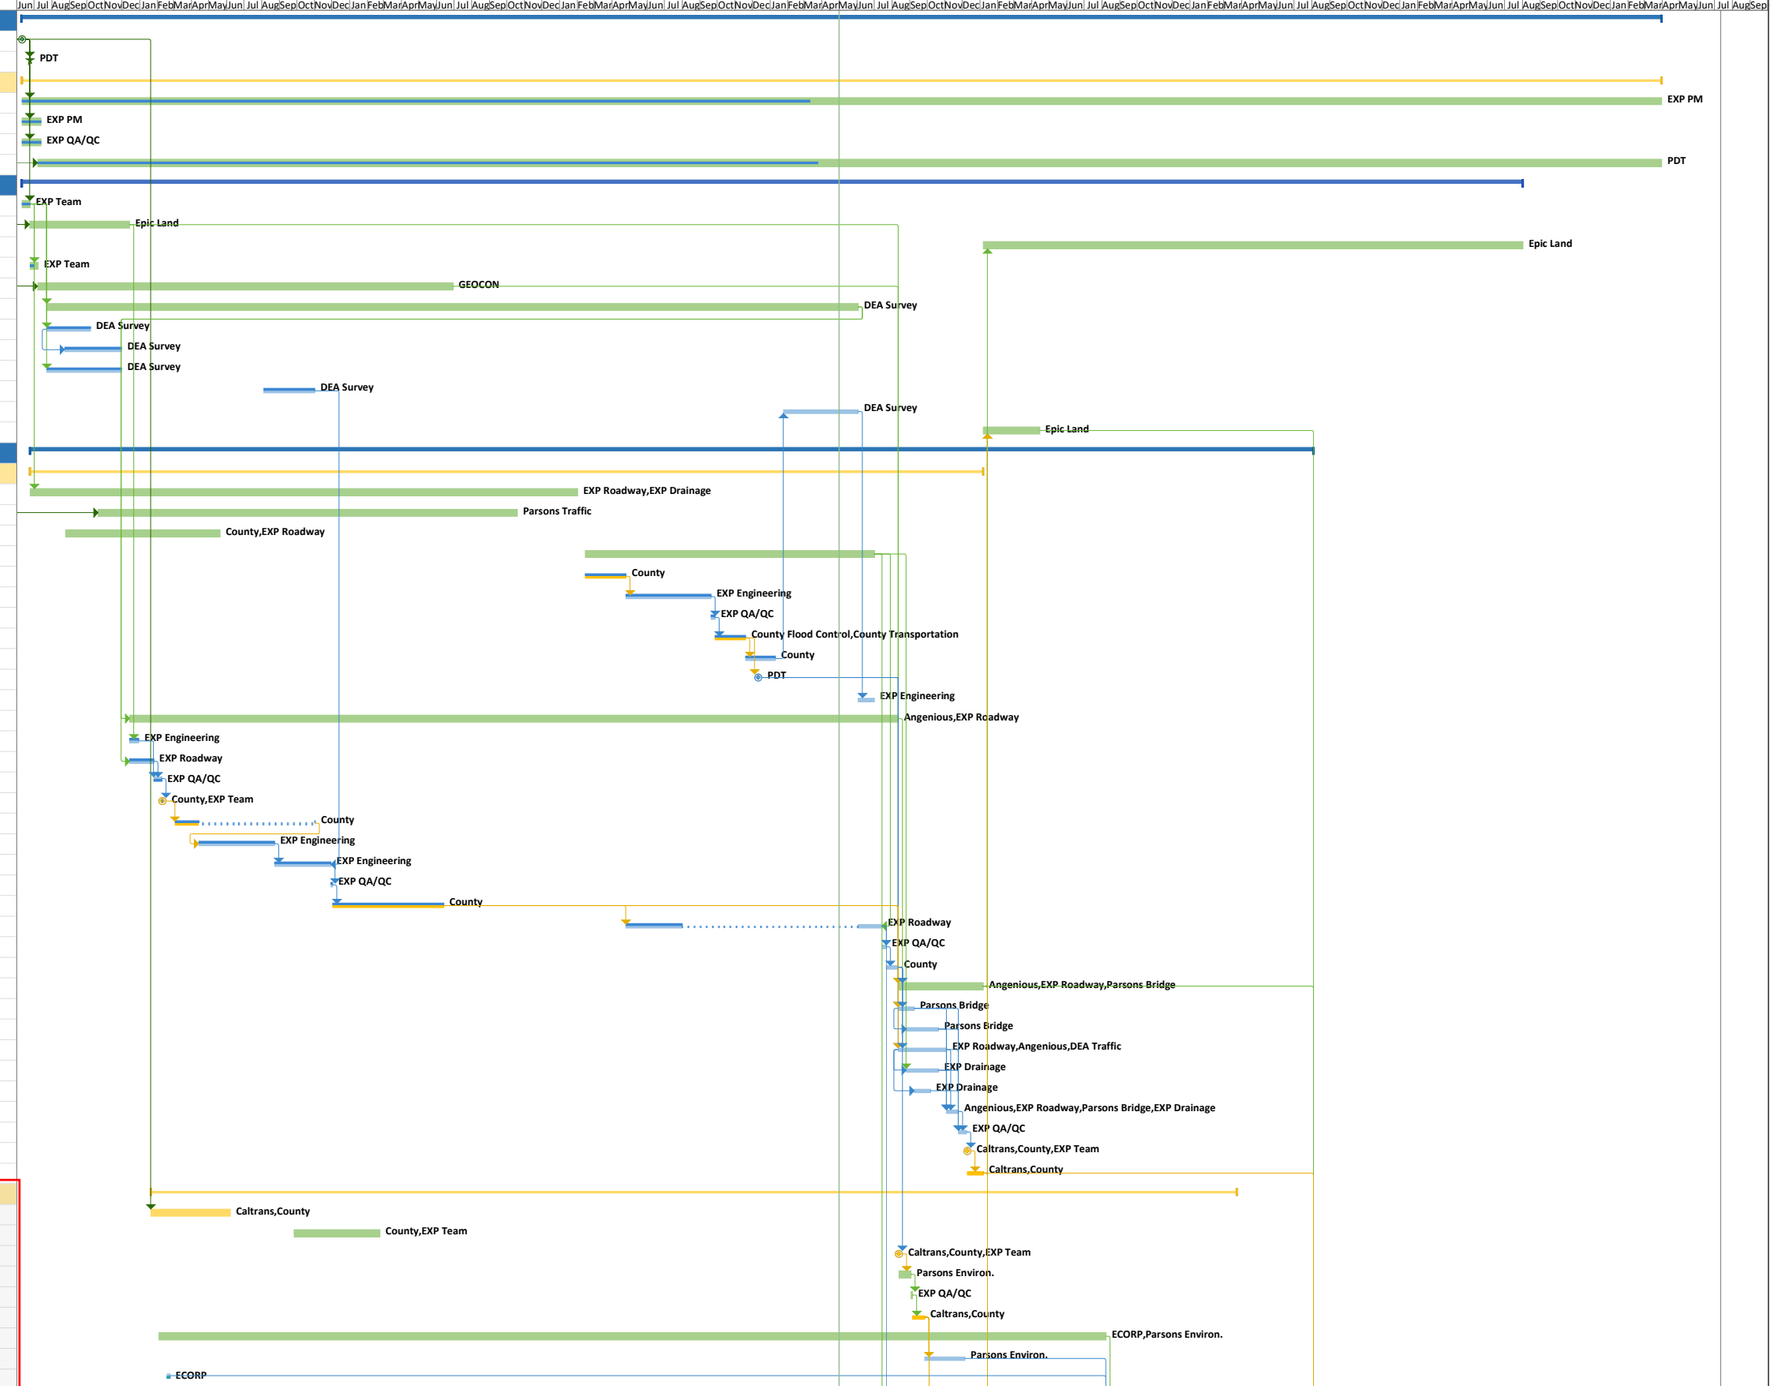

Thu 5/1/25

Phelan Road Widening
Work Order No. H15057
Project Schedule

ID	Task Name	Duration	Start	Finish	% Complete
185	Biological Reconnaissance Surveys	571 days	Thu 2/3/22	Thu 4/11/24	99%
190	Biological Survey Reports	367 days	Fri 3/31/23	Mon 8/26/24	100%
205	Area of Potential Effects (APE)	40 days	Mon 7/14/25	Mon 9/8/25	0%
206	Daytime Bat Habitat Assessment and Memorandum	50 days	Mon 9/8/25	Mon 11/17/25	0%
207	NES Report	98 days	Mon 9/8/25	Thu 1/22/26	0%
208	BA Report	98 days	Mon 9/8/25	Thu 1/22/26	0%
209	Incidental Take Permit Application	219 days	Mon 10/6/25	Fri 8/7/26	0%
210	MGS Habitat Assessment Technical Memorandum and CDFW Negotiations (Optional)	77 days	Mon 12/1/25	Wed 3/18/26	0%
211	MGS Trapping and Report (Optional)	132 days	Mon 1/12/26	Wed 7/15/26	0%
212	Caltrans Noise Study	120 days	Fri 9/26/25	Fri 3/13/26	0%
213	Jurisdictional and Wetland Delineation	97 days	Fri 9/26/25	Tue 2/10/26	0%
214	Cultural and Paleontological Resource Reports	218 days	Fri 9/26/25	Wed 7/29/26	0%
215	Hazardous Materials Study	20 days	Fri 9/26/25	Fri 10/24/25	0%
216	Water Quality Assessment Report (Optional)	50 days	Fri 9/26/25	Fri 12/5/25	0%
217	Floodplain Evaluation Report (Optional)	50 days	Fri 9/26/25	Fri 12/5/25	0%
218	Visual Impact Assessment (Optional)	20 days	Fri 9/26/25	Fri 10/24/25	0%
219	Community Impact Assessment (Optional)	20 days	Fri 9/26/25	Fri 10/24/25	0%
220	QA/QC Review and Revisions	15 days	Fri 8/7/26	Fri 8/28/26	0%
221	County and Caltrans Review - Technical Studies	30 days	Fri 8/28/26	Fri 10/9/26	0%
222	Prepare Draft IS/MND and EA/FONSI	30 days	Fri 10/9/26	Fri 11/20/26	0%
223	QA/QC Review and Revisions	15 days	Fri 11/20/26	Fri 12/11/26	0%
224	County and Caltrans Review - IS/MND and EA/FONSI	20 days	Fri 12/11/26	Fri 1/8/27	0%
225	Address County and Caltrans Comments	20 days	Fri 1/8/27	Fri 2/5/27	0%
226	QA/QC Review and Revisions	10 days	Fri 2/5/27	Fri 2/19/27	0%
227	Circulate Environmental Documents	22 days	Fri 2/19/27	Tue 3/23/27	0%
228	Public Outreach Meeting	1 day	Mon 3/8/27	Tue 3/9/27	0%
229	**Final Environmental Document**	**105 days**	**Tue 3/9/27**	**Tue 8/3/27**	**0%**
230	Address Public Comments and Prepare Final IS/MND and EA	30 days	Tue 3/9/27	Tue 4/20/27	0%
231	QA/QC Review and Revisions	10 days	Tue 4/20/27	Tue 5/4/27	0%
232	County and Caltrans Review - FINAL IS/MND and EA	20 days	Tue 5/4/27	Tue 6/1/27	0%
233	Address County and Caltrans Final Review Comments	20 days	Tue 6/1/27	Tue 6/29/27	0%
234	QA/QC Review and Revisions	5 days	Tue 6/29/27	Tue 7/6/27	0%
235	County and Caltrans Review and Approval - FINAL IS/MND and EA	20 days	Tue 7/6/27	Tue 8/3/27	0%
236	**PLANS, SPECIFICATIONS, AND ESTIMATES (PS&E)**	**1114.4 d**	**Thu 4/3/25**	**Wed 7/11/29**	**0%**
237	**Regulatory Permitting**	**783.4 da**	**Thu 4/3/25**	**Tue 4/4/28**	**0%**
238	Biological Field Surveys	84 days	Thu 4/3/25	Tue 7/29/25	0%
239	Desert Tortoise Survey and Combined DT/BUOW Report	84 days	Thu 4/3/25	Tue 7/29/25	0%
240	Burrowing Owl Surveys and Combined DT/BUOW Report	84 days	Thu 4/3/25	Tue 7/29/25	0%
241	Rare Plant Surveys and Report	84 days	Thu 4/3/25	Tue 7/29/25	0%
242	Prepare Regulatory Permits	30 days	Tue 7/20/27	Tue 8/31/27	0%
243	QA/QC Review and Revisions	5 days	Tue 8/31/27	Tue 9/7/27	0%
244	Regulartory Agency Review and Coordination	150 days	Tue 9/7/27	Tue 4/4/28	0%
245	**Railroad Coordination and Agreements**	**682 days**	**Tue 1/6/26**	**Thu 8/17/28**	**0%**
246	Railroad Coordination and Agreements	682 days	Tue 1/6/26	Thu 8/17/28	0%
254	**Right-of-Way**	**802 days**	**Tue 1/6/26**	**Thu 2/1/29**	**0%**
255	Right-of-Way Requirements Map	75 days	Tue 1/6/26	Tue 4/21/26	0%
262	Legals and Plats	95 days	Tue 1/6/26	Tue 5/19/26	0%
269	Right-of-Way Acquisition	452 days	Tue 5/11/27	Thu 2/1/29	0%
272	**65% PS&E**	**110 days**	**Tue 8/3/27**	**Tue 1/4/28**	**0%**
273	Prepare 65% PS&E	65 days	Tue 8/3/27	Tue 11/2/27	0%
283	QC Review and Revisions	15 days	Tue 11/2/27	Tue 11/23/27	0%
284	County and Caltrans Review - 65% PS&E	30 days	Tue 11/23/27	Tue 1/4/28	0%
285	**95% PS&E**	**87 days**	**Tue 1/4/28**	**Thu 5/4/28**	**0%**
286	Prepare 95% PS&E	40 days	Tue 1/4/28	Tue 2/29/28	0%
288	QA/QC Review and Revisions	15 days	Tue 2/29/28	Tue 3/21/28	0%
289	County and Caltrans Review - 95% PS&E	32 days	Tue 3/21/28	Thu 5/4/28	0%
290	**Final PS&E**	**309 days**	**Thu 5/4/28**	**Wed 7/11/29**	**0%**
291	Prepare Final PS&E Package	30 days	Thu 5/4/28	Thu 6/15/28	0%
293	QA/QC Review and Revisions	10 days	Thu 6/15/28	Thu 6/29/28	0%
294	County and Caltrans Review and Approval - FINAL PS&E	15 days	Thu 6/29/28	Thu 7/20/28	0%
295	Submit RFA Package to Caltrans to Receive E-76	20 days	Thu 3/1/29	Thu 3/29/29	0%
296	Receive E-76 for Construction Allocation	1 day	Thu 3/29/29	Fri 3/30/29	0%
297	Board Approval of PS&E Package	1 day	Fri 4/13/29	Mon 4/16/29	0%
298	Ready-to-List (RTL) and Advertise	30 days	Mon 4/30/29	Mon 6/11/29	0%
299	Award Contract	1 day	Mon 6/11/29	Tue 6/12/29	0%
300	Construction	1 day	Tue 7/10/29	Wed 7/11/29	0%

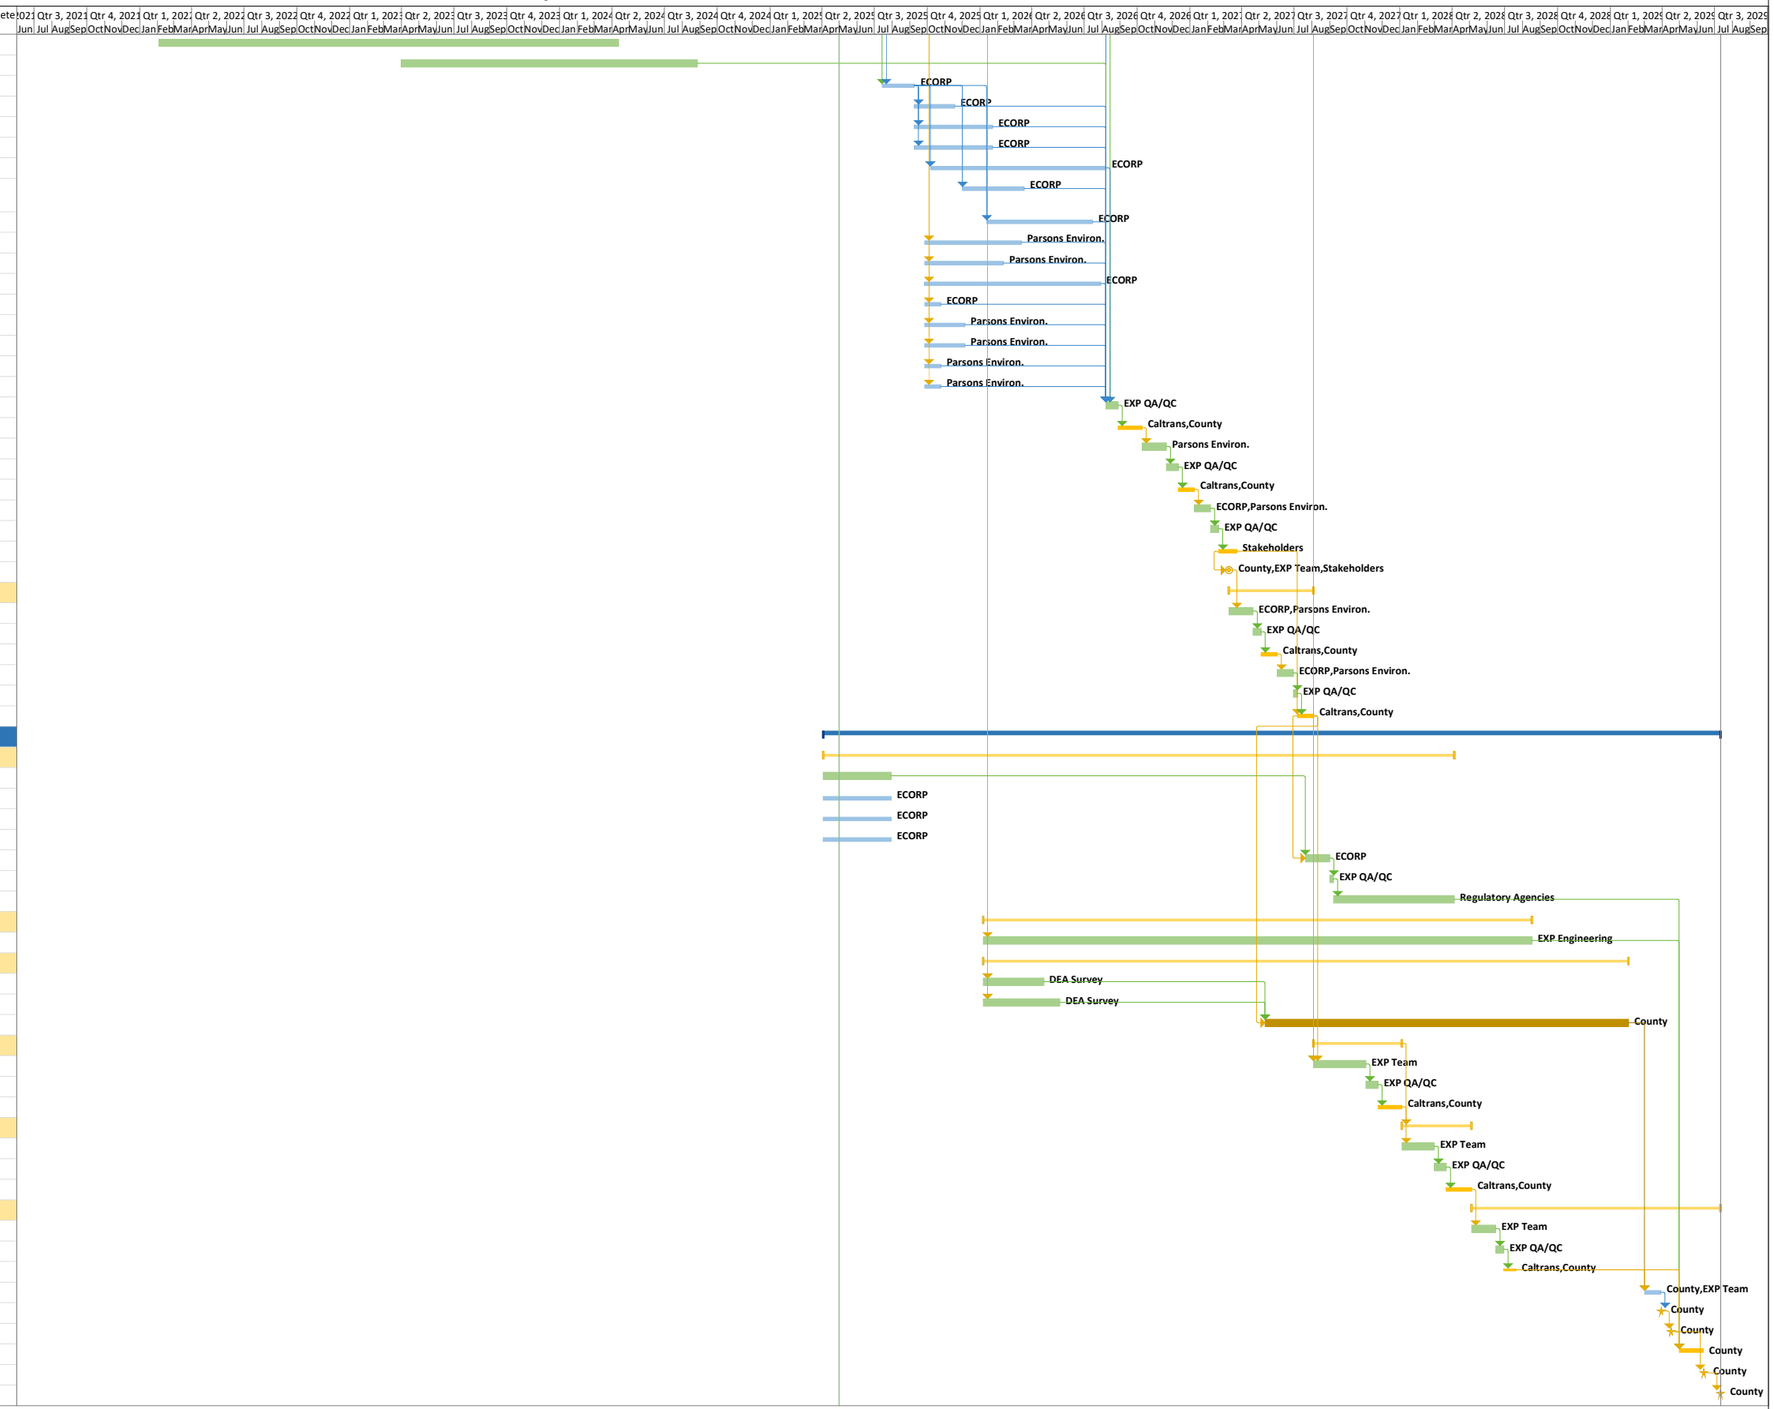

Thu 5/1/25
